


ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
1	Burnaby Hospital Redevelopment Project - BHRP CM	1 day	Fri 5/01/20	Fri 5/01/20															
2	FF&E MANAGEMENT PROCESS																		
3	Financial Close	0 days		Thu 7/29/21														2/17	
4	50% Design Submission Reviewed (50% DD)	0 days		Mon 5/16/22															
5	70% Design Submission Revied	0 days	Mon 11/28/22	Mon 11/28/22															
6	90% Design Submission Reviewed (100% CD)-CM1	1 day	Mon 2/27/23	Mon 2/27/23															
7	90% Informal Design Equipment list freeze -CM2	1 day?	Mon 4/24/23	Mon 4/24/23															
8	90% Formal Design Submission Reviewed-CM2	1 day?	Tue 2/06/24	Tue 2/06/24															
9	100% Formal Design Equipment list freeze -CM2	1 day?	Wed 2/28/24	Wed 2/28/24															
10	100% Design Submission Reviewed (100% CD)	0 days	Wed 4/10/24	Wed 4/10/24															
11	IFC Complete	0 days	Wed 4/10/24	Wed 4/10/24															
12	CM Substantial Completion	1 day	Tue 2/17/26	Tue 2/17/26															
13	1.0 PROJECT MANAGEMENT																		
14	1.1 FURNITURE & EQUIPMENT STEERING COMMITTEE (FE-SC)	1181 days	Mon 8/23/21	Fri 4/03/26															
15	Meeting - kickoff with the Authority to review scope, objectives, schedule, terms and understanding	1 day	Mon 8/23/21	Mon 8/23/21	3FS+15 days														
16	Revise FF&E project schedule and integrate comments	6 mons	Tue 8/24/21	Fri 2/11/22	15														
17	Submission of Baseline FF&E Schedule and supporting documentation	0 days		Fri 2/11/22	16														
18	Monthly Furniture & Equipment Steering Committee Meetings - to monitor and review FF&E activities (CEC)	59 mons	Tue 8/24/21	Fri 4/03/26	15														
19	2.0 PLANNING & DESIGN PHASE																		
20	2.1 FF&E DATABASE MANAGEMENT	1027 days	Wed 3/18/20	Wed 4/10/24															
21	Authority to handover FF&E list - database setup & coordination with the Authority's team	3 mons	Tue 8/24/21	Wed 11/17/21	15														
22	Develop database reporting and utility data reports	3 mons	Thu 11/18/21	Fri 2/11/22	21														
23	Issue FF&E List & Reports for design coordination (BASELINE FF&E LIST)	0 days	Fri 2/11/22	Fri 2/11/22	22														
24	Organize cuthseets and refine database reporting and utility data reports	6 mons	Mon 2/14/22	Mon 8/08/22	23														
25	Issue FF&E List & Reports for 50% Design Submission (50% DD)	0 days	Thu 4/14/22	Thu 4/14/22	4FF-1 mon														
26	Validate FF&E database list based on comments from Authority and User Group meetings	1.5 mons	Wed 3/18/20	Thu 4/30/20	27SF														
27	Issue FF&E List & Reports for 90% Design Submission (50% CD)	0 days	Fri 5/01/20	Fri 5/01/20															
28	Update FF&E database list based on comments from Authority and User Group meetings	1.5 mons	Wed 1/31/24	Tue 3/12/24	29SF														
29	Issue FF&E List & Reports for 100% Design Submission (100% CD)	0 days	Tue 3/12/24	Tue 3/12/24	10FF-1 mon														
30	Final updates to FF&E database list based on comments from Authority and User Group meetings	1.5 mons	Wed 2/28/24	Wed 4/10/24	31SF														
31	Issue Final FF&E List & Reports for Procurement	0 days	Wed 4/10/24	Wed 4/10/24	11FF														
32	3.0 RENOVATION PERIODS (by Area and Phase)		Fri 5/01/20																
33	3.1 RENOVATION PERIOD BY AREA	685 days	Mon 5/15/23	Mon 1/12/26															
34	Cardiac Rehab Renovation period (SFB L1)	231 days	Wed 3/20/24	Tue 2/11/25															
35	Cardiac Rehab Final Clean	2 days	Wed 11/27/24	Thu 11/28/24															
36	Cardiac Rehab Move-in Date	1 day	Tue 1/14/25	Tue 1/14/25															
37	Pharmacy Renovation Period (SFB L2)	447 days	Thu 6/22/23	Tue 3/18/25															
38	Pharmacy Final Clean	2 days	Fri 9/27/24	Mon 9/30/24															
39	Pharmacy Move-in Date	1 day	Tue 1/21/25	Tue 1/21/25															
40	HR Renovation Period (NT L1)	195 days	Mon 5/15/23	Wed 2/14/24															
41	HR Final Clean	1 day	Wed 1/10/24	Wed 1/10/24															
42	HR Move-In Date	5 days	Thu 2/01/24	Wed 2/07/24															
43	IHR Renovation Period (SFB L2)	124 days	Wed 4/09/25	Tue 9/30/25															
44	IHR Final Clean	2 days	Mon 9/29/25	Tue 9/30/25															
45	IHR Move-in Date	0 days	Thu 11/13/25	Thu 11/13/25															
46	Emergency Renovation Period (SFB L3)	241 days	Tue 2/04/25	Mon 1/12/26															
47	Emergency Final Clean	2 days	Fri 11/28/25	Mon 12/01/25															
48	Emergency Move-in	2 days	Fri 1/09/26	Mon 1/12/26															
49	FMO Offices /Workshop Renovation Period (SFB L2)	135 days	Thu 5/08/25	Thu 11/13/25															
50	FMO Offices /Workshop Final Clean	2 days	Wed 11/12/25	Thu 11/13/25															
51	FMO Offices/Workshop Move-in	0 days	Mon 1/05/26	Mon 1/05/26															
52	3.2 SFB L4 RENOVATION PERIOD BY PHASE (Not In Contract)	911 days	Thu 4/03/25	Tue 10/10/28															
53	Phase 1A - OR Registration Renovation Period	438 days	Thu 4/03/25	Mon 12/14/26															
54	Phase 1A - OR Registration Final Clean Dates	3 days	Mon 8/10/26	Wed 8/12/26															
55	Phase 1A - OR Registration Move-In Dates	31 days	Mon 11/02/26	Mon 12/14/26															
56	Phase 1B- ORs Renovation Period	438 days	Thu 4/03/25	Mon 12/14/26															
57	Phase 1B - OR Renovation Final Clean Dates	3 days	Wed 3/03/27	Fri 3/05/27															
58	Phase 1B - OR Renovation Move-In Dates	42 days	Thu 7/15/27	Fri 9/10/27															
59	Phase 1C - Procedure Rooms Renovation Period	402 days	Thu 4/03/25	Fri 10/23/26															
60	Phase 1C - Procedure Rooms - Final Clean Dates	3 days	Wed 5/20/26	Fri 5/22/26															
61	Phase 1C - Procedure Rooms Move-In Dates	42 days	Thu 8/27/26	Fri 10/23/26															
62	Phase 2A/2B- PreOp Post Stretcher Bay Renovation Period	473 days	Tue 12/15/26	Tue 10/10/28															
63	Phase 2A/2B- PreOp Post Stretcher Bay Renovation Period Final Clean	4 days	Thu 5/04/28	Tue 5/09/28															
64	Phase 2A/2B- PreOp Post Stretcher Bay Renovation Period Move-In Date	42 days	Mon 8/14/28	Tue 10/10/28															
65	Phase 2A/2B- Staff Change Room Renovation Period	241 days	Thu 4/03/25	Wed 3/11/26															
66	Phase 2A/2B- Staff Change Room Renovation Period Final Clean	5 days	Mon 12/01/25	Fri 12/05/25															
67	Phase 2A/2B- Staff Change Room Renovation Period Move-In Date	10 days	Thu 2/26/26	Wed 3/11/26															


ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
68	Phase 3- New Pre-Post OP Stretcher Bay/Care Team Station Renovation Period	634 days	Mon 12/15/25	Mon 5/29/28															
69	Phase 3- New Pre-Post OP Stretcher Bay/Care Team Station Renovation Period Final Clean	5 days	Mon 12/06/27	Fri 12/10/27															
70	Phase 3- New Pre-Post OP Stretcher Bay/Care Team Station Renovation Period Final Clean Move-In Date	42 days	Fri 3/31/28	Mon 5/29/28															
71	4.0 PROCUREMENT PHASE (PHARMACY - SFB L2)																		
72	4.1 Pharmacy - In Contract (Category 4,5)- By EDDB	673 days	Wed 5/25/22	Tue 1/07/25															
73	Procurement Strategy and Administration	300 days	Fri 9/16/22	Mon 11/13/23															
74	Evaluation Committee Meeting #1 Prep	4 wks	Fri 9/16/22	Fri 10/14/22															
75	Evaluation Committee Meeting #1 (Date TBC by FHA)	1 day	Mon 10/17/22	Mon 10/17/22	74														
76	Incorporate Feedback from Evaluation Meeting #1	15 days	Tue 10/18/22	Mon 11/07/22	75														
77	Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development) by FHA	15 days	Tue 11/08/22	Mon 11/28/22	76														
78	Evaluation Committee Meeting #2 (Date TBC by FHA)	1 day	Wed 7/05/23	Wed 7/05/23	77														
79	Incorporate Feedback from Evaluation Meeting #2	5 days	Thu 7/06/23	Wed 7/12/23	78														
80	RFP Documents Preparation by ED FED	11 wks	Thu 7/13/23	Wed 9/27/23	79														
81	Release RFP Document Draft to FHA by ED FED	0 days	Wed 9/27/23	Wed 9/27/23	80														
82	Owner Review of Draft documents	1 wk	Thu 9/28/23	Wed 10/04/23	81														
83	RFP Documents Preparation Meeting#1 - Review RFP draft (Date TBC by FHA)	1 day	Thu 10/05/23	Thu 10/05/23	82														
84	Incorporate Feedback from RFP Documents Preparation Meeting#1	1 wk	Fri 10/06/23	Thu 10/12/23	83														
85	RFP Documents Preparation Meeting#2 - Refine RFP draft (Date TBC by FHA)	1 day	Fri 10/13/23	Fri 10/13/23	84														
86	Incorporate Feedback from RFP Documents Preparation Meeting#2	1 wk	Mon 10/16/23	Fri 10/20/23	85														
87	RFP Documents Preparation Meeting#3 - Finalize RFP draft (Date TBC by FHA)	1 day	Mon 10/23/23	Mon 10/23/23	86														
88	Incorporate Feedback from RFP Documents Preparation Meeting#3	1 wk	Tue 10/24/23	Mon 10/30/23	87														
89	Approval of all Documentation incl Final Specs, D&C Drawings, etc	2 wks	Tue 10/31/23	Mon 11/13/23	88														
90	Tender Period	30 days	Tue 11/14/23	Wed 12/27/23															
91	Open Tender Period (RFP/RFQ/Direct Awards)	15 days	Tue 11/14/23	Mon 12/04/23	89														
92	Tender Process Close	0 days	Mon 12/04/23	Mon 12/04/23	91														
93	Proposal Completeness Check	2 wks	Tue 12/05/23	Mon 12/18/23	92														
94	Technical Compliance Check	2 wks	Tue 12/05/23	Mon 12/18/23	92														
95	Financial Analysis	2 wks	Tue 12/05/23	Mon 12/18/23	92														
96	Financial Analysis Complete	0 days	Mon 12/18/23	Mon 12/18/23	95														
97	Prepare Procurement Summary Report	1 wk	Tue 12/19/23	Wed 12/27/23	96														
98	Submit Procurement Summary Report to Owner (Short list) by ED FED	0 days	Wed 12/27/23	Wed 12/27/23	97														
99	RFP Evaluation Period	33 days	Thu 12/28/23	Tue 2/13/24															
100	Owner Review of Vendor Bids and Analysis by FHA	2 wks	Thu 12/28/23	Thu 1/11/24	98														
101	Evaluation Committee Meeting #3 for Vendor Shortlist (Date TBD)	1 day	Fri 1/12/24	Fri 1/12/24	100														
102	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	4 wks	Thu 12/28/23	Thu 1/25/24	97														
103	Owner Internal Evaluation Meeting (Technical, Clinical, Financial Analysis)	2 wks	Fri 1/26/24	Thu 2/08/24	102														
104	Evaluation Committee Meeting #4 for Final Vendor Selection (Date TBD)	1 day	Fri 2/09/24	Fri 2/09/24	103														
105	Submit Final Procurement Report to Owner for Sign Off by ED FED	1 day	Mon 2/12/24	Mon 2/12/24	104														
106	Owner Sign Off (Preferred Vendor)	1 day	Tue 2/13/24	Tue 2/13/24	105														
107	Contract Administration	30 days	Wed 2/14/24	Tue 3/26/24															
108	Final Negotiation with Successful Bidder by ED FED	1 wk	Wed 2/14/24	Tue 2/20/24	106														
109	Development of Equipment Configuration with ED FED	1 wk	Wed 2/21/24	Tue 2/27/24	108														
110	Development of PO Documentations by EDDB	10 days	Wed 2/28/24	Tue 3/12/24	109														
111	Collection of Signatures for Approval (Senior Leadership)	2 wks	Wed 3/13/24	Tue 3/26/24	110														
112	PO Issued by EDDB	0 days	Tue 3/26/24	Tue 3/26/24	111														
113	Final Design Coordination	40 days	Wed 2/21/24	Tue 4/16/24															
114	Coordination of Final Shop Drawing with Vendor	3 wks	Wed 2/21/24	Tue 3/12/24	108														
115	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Tue 3/12/24	Tue 3/12/24	114														
116	Shop Drawing Review by EDDB	2 wks	Wed 3/13/24	Tue 3/26/24	115														
117	Final Shop Drawing and Building Services Review Complete	0 days	Tue 3/26/24	Tue 3/26/24	116														
118	Final Shop Drawing Owner Review Period	15 days	Wed 3/27/24	Tue 4/16/24	117														
119	Approval of Final Shop Drawings by Owner	0 days	Tue 4/16/24	Tue 4/16/24	118														
120	Delivery & Instalation	170 days	Wed 4/17/24	Wed 12/11/24															
121	Manufacturing & Site Coordination	140 days	Wed 4/17/24	Wed 10/30/24															
122	Fabrication and Confirm Delivery Room Readiness	23 wks	Wed 4/17/24	Wed 9/25/24	119														
123	Assembly, Installation, Set up and Testing (tied to room readiness dates)	5 wks	Thu 9/26/24	Wed 10/30/24	122														
124	Installation Complete- Issue Notice to Contracting Authority	0 days	Wed 10/30/24	Wed 10/30/24	123														
125	Vendor Closeout	30 days	Thu 10/31/24	Wed 12/11/24															
126	Contracting Authority Technical Acceptance testing/training	1 wk	Thu 10/31/24	Wed 11/06/24	124														
127	Collection and handover of Product Information(warranty, test reports, etc.)	1 wk	Thu 11/07/24	Wed 11/13/24	126														
128	Deficiencies & Remediation Period	4 wks	Thu 10/31/24	Wed 11/27/24	126SS														
129	Technical Acceptance and Training Complete	0 days	Wed 11/27/24	Wed 11/27/24	128														
130	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	2 wks	Thu 11/28/24	Wed 12/11/24	129														
131	FF&E Complete - Contracting Authority Sign Off	0 days	Wed 12/11/24	Wed 12/11/24	130														
132	4.2 Pharmacy- Not In Contract (Category 1,2,3)- procurement by By FHA	657 days	Wed 5/25/22	Wed 12/11/24															
133	Procurement Strategy and Administration by FHA	255 days	Wed 5/25/22	Tue 5/23/23															

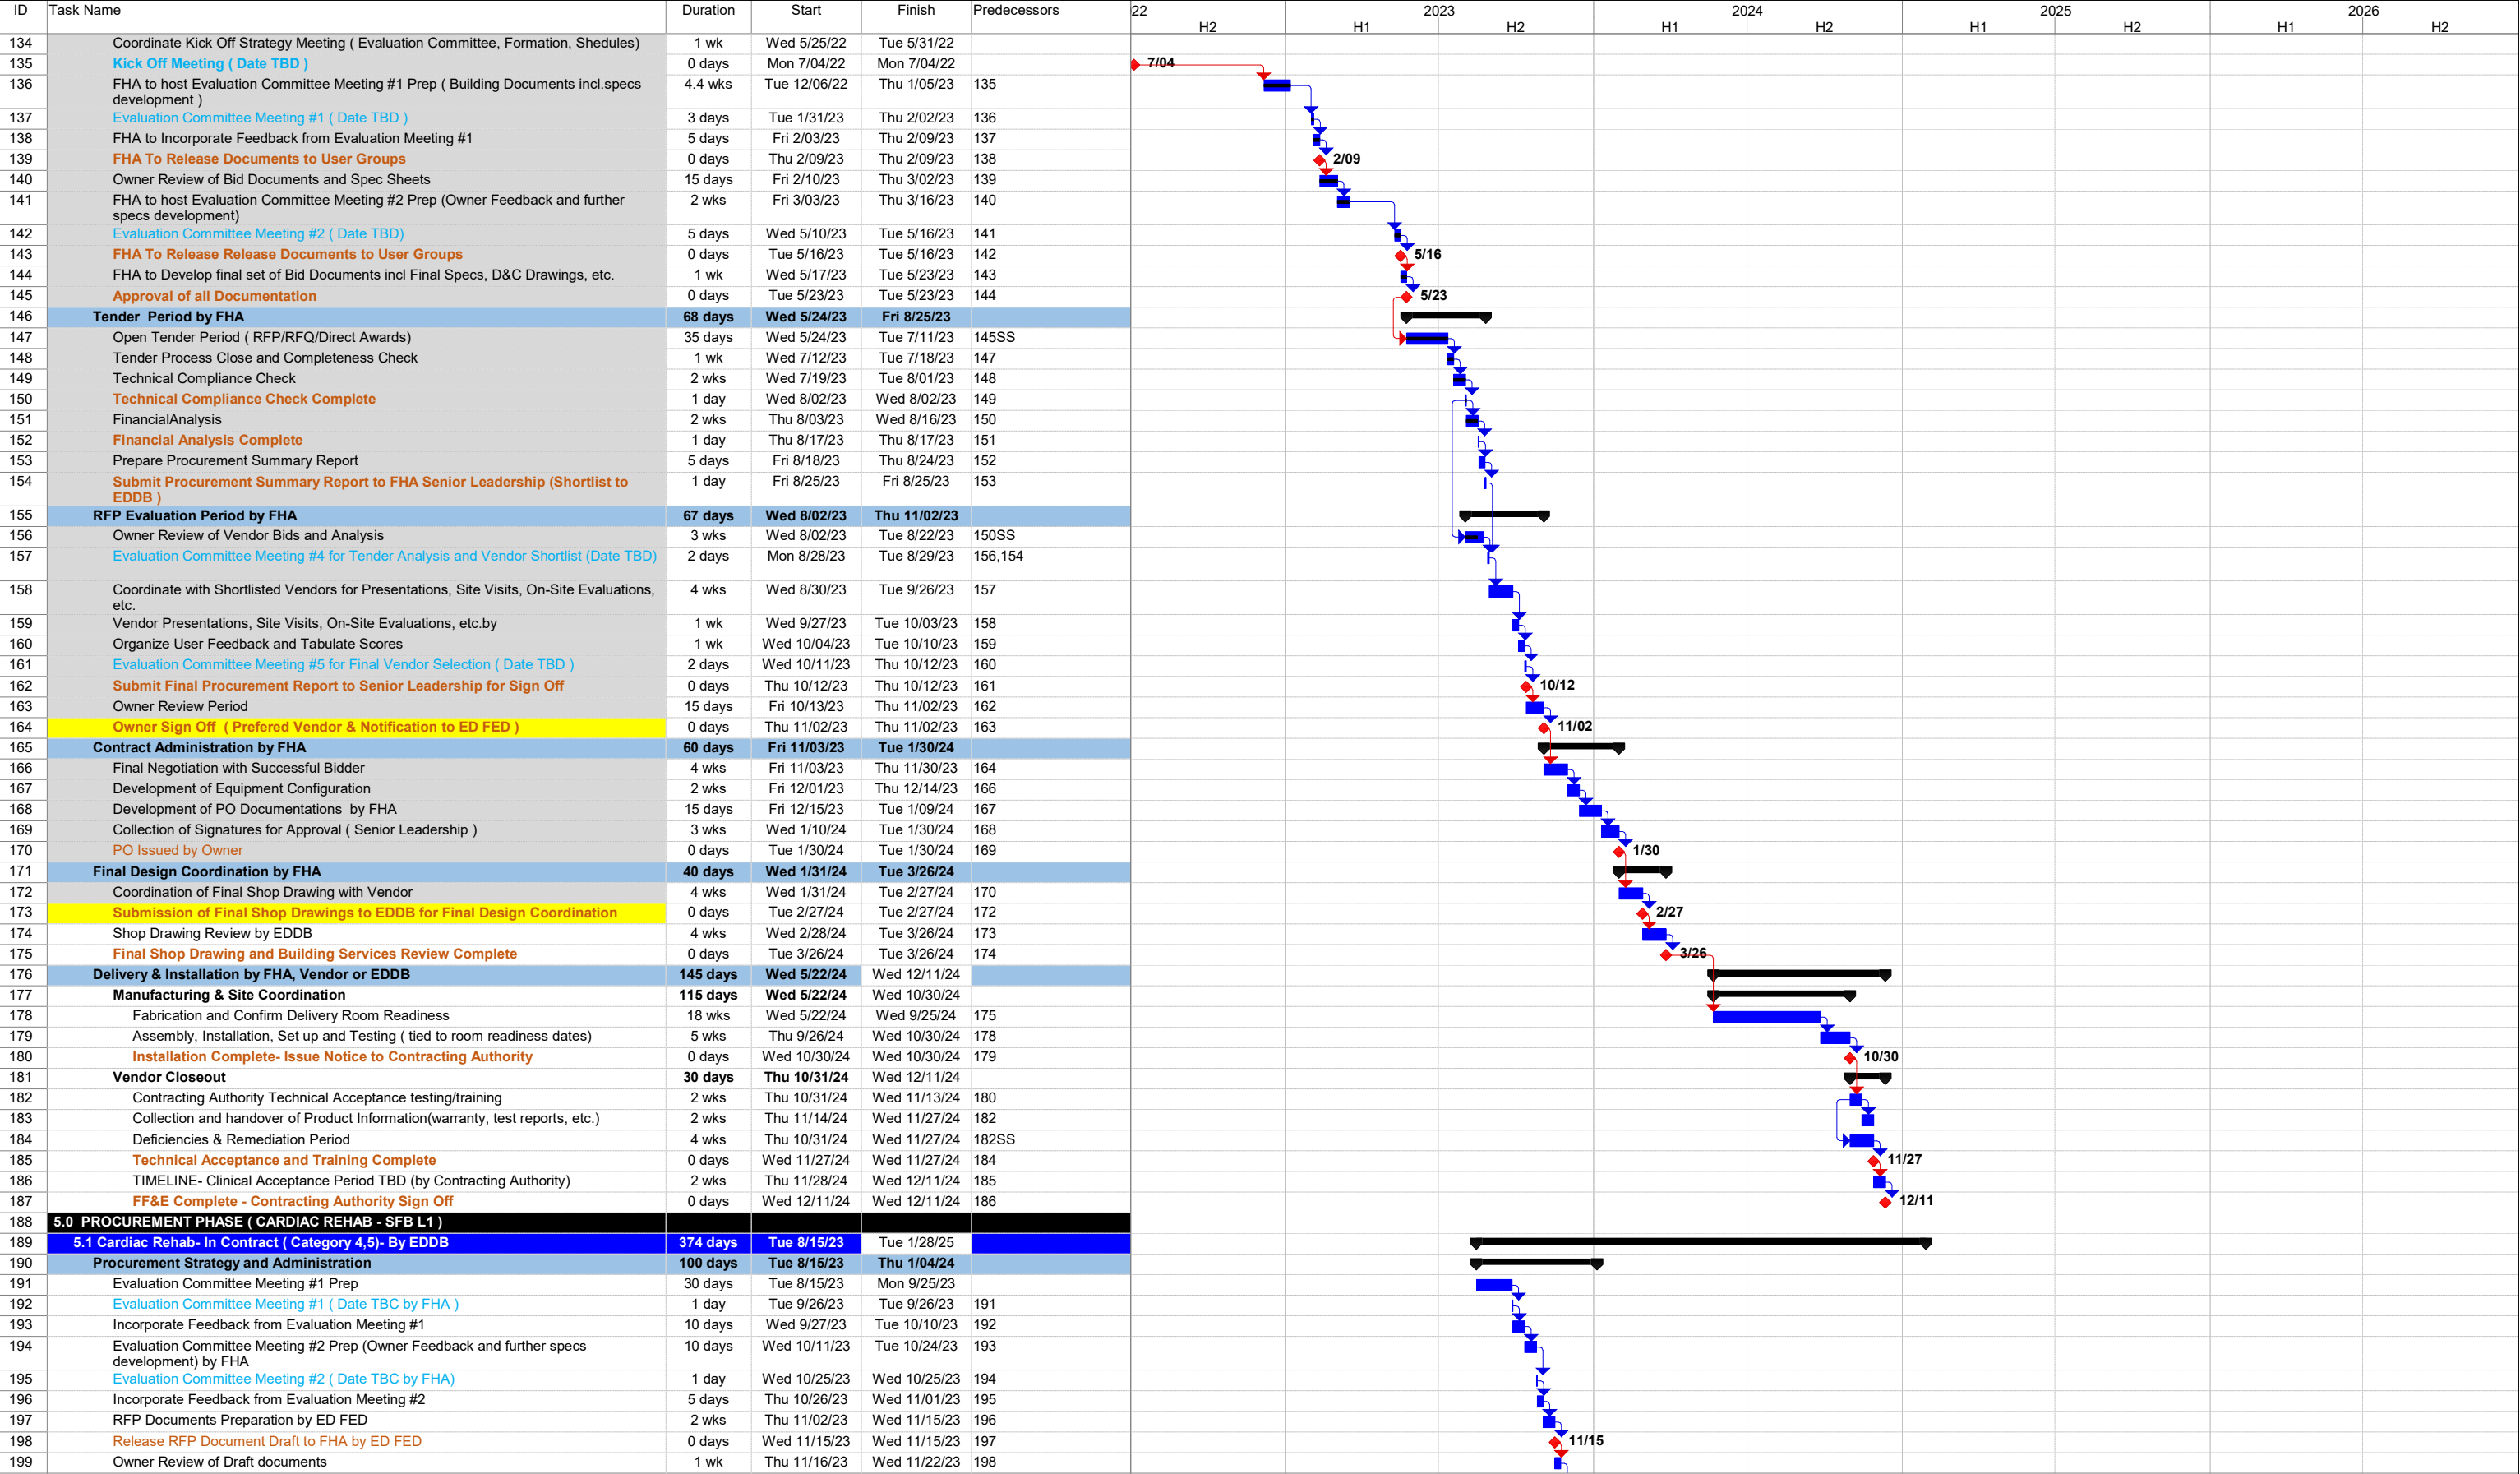

ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
200	RFP Documents Preparation Meeting#1 - Review RFP draft (Date TBC by FHA)	1 day	Thu 11/23/23	Thu 11/23/23	199														
201	Incorporate Feedback from RFP Documents Preparation Meeting#1	1 wk	Fri 11/24/23	Thu 11/30/23	200														
202	RFP Documents Preparation Meeting#2 - Refine RFP draft (Date TBC by FHA)	1 day	Fri 12/01/23	Fri 12/01/23	201														
203	Incorporate Feedback from RFP Documents Preparation Meeting#2	1 wk	Mon 12/04/23	Fri 12/08/23	202														
204	RFP Documents Preparation Meeting#3 - Finalize RFP draft (Date TBC by FHA)	1 day	Mon 12/11/23	Mon 12/11/23	203														
205	Incorporate Feedback from RFP Documents Preparation Meeting#3	1 wk	Tue 12/12/23	Mon 12/18/23	204														
206	Approval of all Documentation incl Final Specs, D&C Drawings, etc	2 wks	Tue 12/19/23	Thu 1/04/24	205														
207	Tender Period	30 days	Fri 1/05/24	Thu 2/15/24															
208	Open Tender Period (RFP/RFQ/Direct Awards)	15 days	Fri 1/05/24	Thu 1/25/24	206														
209	Tender Process Close	0 days	Thu 1/25/24	Thu 1/25/24	208														
210	Proposal Completeness Check	2 wks	Fri 1/26/24	Thu 2/08/24	209														
211	Technical Compliance Check	2 wks	Fri 1/26/24	Thu 2/08/24	209														
212	Financial Analysis	2 wks	Fri 1/26/24	Thu 2/08/24	209														
213	Financial Analysis Complete	0 days	Thu 2/08/24	Thu 2/08/24	212														
214	Prepare Procurement Summary Report	1 wk	Fri 2/09/24	Thu 2/15/24	213														
215	Submit Procurement Summary Report to Owner (Short list) by ED FED	0 days	Thu 2/15/24	Thu 2/15/24	214														
216	RFP Evaluation Period	44 days	Fri 2/16/24	Wed 4/17/24															
217	Owner Review of Vendor Bids and Analysis by FHA	2 wks	Fri 2/16/24	Thu 2/29/24	215														
218	Evaluation Committee Meeting #3 for Vendor Shortlist (Date TBD)	1 day	Fri 3/01/24	Fri 3/01/24	215,217														
219	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	4 wks	Mon 3/04/24	Fri 3/29/24	218														
220	Owner Internal Evaluation Meeting (Technical, Clinical, Financial Analysis)	2 wks	Mon 4/01/24	Fri 4/12/24	219														
221	Evaluation Committee Meeting #4 for Final Vendor Selection (Date TBD)	1 day	Mon 4/15/24	Mon 4/15/24	220														
222	Submit Final Procurement Report to Owner for Sign Off by ED FED	1 day	Tue 4/16/24	Tue 4/16/24	221														
223	Owner Sign Off (Preferred Vendor)	1 day	Wed 4/17/24	Wed 4/17/24	222														
224	Contract Administration	30 days	Thu 4/18/24	Wed 5/29/24															
225	Final Negotiation with Successful Bidder by ED FED	1 wk	Thu 4/18/24	Wed 4/24/24	223														
226	Development of Equipment Configuration with ED FED	1 wk	Thu 4/25/24	Wed 5/01/24	225														
227	Development of PO Documentations by EDDB	10 days	Thu 5/02/24	Wed 5/15/24	226														
228	Collection of Signatures for Approval (Senior Leadership)	2 wks	Thu 5/16/24	Wed 5/29/24	227														
229	PO Issued by EDDB	0 days	Wed 5/29/24	Wed 5/29/24	228														
230	Final Design Coordination	30 days	Thu 5/30/24	Thu 7/11/24															
231	Coordination of Final Shop Drawing with Vendor	2 wks	Thu 5/30/24	Wed 6/12/24	229														
232	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Wed 6/12/24	Wed 6/12/24	231														
233	Shop Drawing Review by EDDB	2 wks	Thu 6/13/24	Wed 6/26/24	232														
234	Final Shop Drawing and Building Services Review Complete	0 days	Wed 6/26/24	Wed 6/26/24	233														
235	Final Shop Drawing Owner Review Period	10 days	Thu 6/27/24	Thu 7/11/24	234														
236	Approval of Final Shop Drawings by Owner	0 days	Thu 7/11/24	Thu 7/11/24	235														
237	Delivery & Instalation	140 days	Fri 7/12/24	Tue 1/28/25															
238	Manufacturing & Site Coordination	120 days	Fri 7/12/24	Mon 12/30/24															
239	Fabrication and Confirm Delivery Room Readiness	20 wks	Fri 7/12/24	Thu 11/28/24	236														
240	Assembly, Installation, Set up and Testing (tied to room readiness dates)	4 wks	Fri 11/29/24	Mon 12/30/24	239														
241	Installation Complete- Issue Notice to Contracting Authority	0 days	Mon 12/30/24	Mon 12/30/24	240														
242	Vendor Closeout	20 days	Tue 12/31/24	Tue 1/28/25															
243	Contracting Authority Technical Acceptance testing/training	1 wk	Tue 12/31/24	Tue 1/07/25	241														
244	Collection and handover of Product Information(warranty, test reports, etc.)	1 wk	Wed 1/08/25	Tue 1/14/25	243														
245	Deficiencies & Remediation Period	2 wks	Tue 12/31/24	Tue 1/14/25	243SS														
246	Technical Acceptance and Training Complete	0 days	Tue 1/14/25	Tue 1/14/25	245														
247	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	2 wks	Wed 1/15/25	Tue 1/28/25	246														
248	FF&E Complete - Contracting Authority Sign Off	0 days	Tue 1/28/25	Tue 1/28/25	247														
249	5.2 Cardiac Rehab-Not In Contract (Category 1,2,3)- procurement by By FHA	706 days	Mon 5/16/22	Thu 2/13/25															
250	Procurement Strategy and Administration by FHA	286 days	Mon 5/16/22	Tue 6/27/23															
251	Coordinate Kick Off Strategy Meeting (Evaluation Committee, Formation, Shedules)	1 wk	Mon 5/16/22	Fri 5/20/22															
252	Kick Off Meeting (Date TBD)	0 days	Mon 7/04/22	Mon 7/04/22															
253	FHA to host Evaluation Committee Meeting #1 Prep (Building Documents incl.specs development)	2 wks	Thu 9/01/22	Thu 9/15/22	252														
254	Evaluation Committee Meeting #1 (Date TBD)	3 days	Tue 5/16/23	Thu 5/18/23	253														
255	FHA to Incorporate Feedback from Evaluation Meeting #1	5 days	Fri 5/19/23	Thu 5/25/23	254														
256	FHA To Release Documents to User Groups	0 days	Thu 5/25/23	Thu 5/25/23	255														
257	Owner Review of Bid Documents and Spec Sheets	10 days	Fri 5/26/23	Thu 6/08/23	256														
258	FHA to host Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development)	1 wk	Fri 6/09/23	Thu 6/15/23	257														
259	Evaluation Committee Meeting #2 (Date TBD)	3 days	Fri 6/16/23	Tue 6/20/23	258														
260	FHA To Release Release Documents to User Groups	0 days	Tue 6/20/23	Tue 6/20/23	259														
261	FHA to Develop final set of Bid Documents incl Final Specs, D&C Drawings, etc.	1 wk	Wed 6/21/23	Tue 6/27/23	260														
262	Approval of all Documentation	0 days	Tue 6/27/23	Tue 6/27/23	261														
263	Tender Period by FHA	55 days	Wed 6/28/23	Tue 9/12/23															
264	Open Tender Period (RFP/RFQ/Direct Awards)	35 days	Wed 6/28/23	Tue 8/15/23	262SS														
265	Tender Process Close and Completeness Check	1 wk	Wed 8/16/23	Tue 8/22/23	264														
266	Technical Compliance Check	1 wk	Wed 8/23/23	Tue 8/29/23	265														
267	Technical Compliance Check Complete	0 days	Tue 8/29/23	Tue 8/29/23	266														

ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
268	FinancialAnalysis	1 wk	Wed 8/30/23	Tue 9/05/23	267														
269	Financial Analysis Complete	0 days	Tue 9/05/23	Tue 9/05/23	268														
270	Prepare Procurement Summary Report	5 days	Wed 9/06/23	Tue 9/12/23	269														
271	Submit Procurement Summary Report to FHA Senior Leadership (Shortlist to EDDB)	0 days	Tue 9/12/23	Tue 9/12/23	270														
272	RFP Evaluation Period by FHA	49 days	Wed 8/30/23	Mon 11/06/23															
273	Owner Review of Vendor Bids and Analysis by FHA	3 wks	Wed 8/30/23	Tue 9/19/23	267SS														
274	Evaluation Committee Meeting #4 for Tender Analysis and Vendor Shortlist (Date TBD)	2 days	Wed 9/20/23	Thu 9/21/23	271,273														
275	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	2 wks	Fri 9/22/23	Thu 10/05/23	274														
276	Vendor Presentations, Site Visits, On-Site Evaluations, etc.by	1 wk	Fri 10/06/23	Thu 10/12/23	275														
277	Organize User Feedback and Tabulate Scores	1 wk	Fri 10/13/23	Thu 10/19/23	276														
278	Evaluation Committee Meeting #5 for Final Vendor Selection (Date TBD)	2 days	Fri 10/20/23	Mon 10/23/23	277														
279	Submit Final Procurement Report to Senior Leadership for Sign Off	0 days	Mon 10/23/23	Mon 10/23/23	278														
280	Owner Review Period	10 days	Tue 10/24/23	Mon 11/06/23	279														
281	Owner Sign Off (Preferred Vendor & Notification to ED FED)	0 days	Mon 11/06/23	Mon 11/06/23	280														
282	Contract Administration by FHA	45 days	Tue 11/07/23	Thu 1/11/24															
283	Final Negotiation with Successful Bidder	3 wks	Tue 11/07/23	Mon 11/27/23	281														
284	Development of Equipment Configuration	2 wks	Tue 11/28/23	Mon 12/11/23	283														
285	Development of PO Documentations by FHA	15 days	Tue 12/12/23	Thu 1/04/24	284														
286	Collection of Signatures for Approval (Senior Leadership)	1 wk	Fri 1/05/24	Thu 1/11/24	285														
287	PO Issued by Owner	0 days	Thu 1/11/24	Thu 1/11/24	286														
288	Final Design Coordination by FHA	35 days	Fri 1/12/24	Thu 2/29/24															
289	Coordination of Final Shop Drawing with Vendor	4 wks	Fri 1/12/24	Thu 2/08/24	287														
290	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Thu 2/08/24	Thu 2/08/24	289														
291	Shop Drawing Review by EDDB	3 wks	Fri 2/09/24	Thu 2/29/24	290														
292	Final Shop Drawing and Building Services Review Complete	0 days	Thu 2/29/24	Thu 2/29/24	291														
293	Delivery & Installation by FHA, Vendor or EDDB	140 days	Fri 7/12/24	Tue 1/28/25															
294	Manufacturing & Site Coordination	120 days	Fri 7/12/24	Mon 12/30/24															
295	Fabrication and Confirm Delivery Room Readiness	20 wks	Fri 7/12/24	Thu 11/28/24	292														
296	Assembly, Installation, Set up and Testing (tied to room readiness dates)	4 wks	Fri 11/29/24	Mon 12/30/24	295														
297	Installation Complete- Issue Notice to Contracting Authority	0 days	Mon 12/30/24	Mon 12/30/24	296														
298	Vendor Closeout	20 days	Tue 12/31/24	Tue 1/28/25															
299	Contracting Authority Technical Acceptance testing/training	1 wk	Tue 12/31/24	Tue 1/07/25	297														
300	Collection and handover of Product Information(warranty, test reports, etc.)	1 wk	Wed 1/08/25	Tue 1/14/25	299														
301	Deficiencies & Remediation Period	2 wks	Tue 12/31/24	Tue 1/14/25	299SS														
302	Technical Acceptance and Training Complete	0 days	Tue 1/14/25	Tue 1/14/25	301														
303	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	2 wks	Wed 1/15/25	Tue 1/28/25	302														
304	FF&E Complete - Contracting Authority Sign Off	0 days	Tue 1/28/25	Tue 1/28/25	303														
305	6.0 PROCUREMENT PHASE (HUMAN RESOURCES - NT L1)																		
306	6.1 Human Resources- In Contract (Category 4,5)- By EDDB (Fast-tracked)	391 days	Wed 5/25/22	Wed 11/29/23															
307	Procurement Strategy and Administration	41 days	Tue 8/15/23	Tue 10/10/23															
308	Evaluation Committee Meeting #1 Prep	15 days	Tue 8/15/23	Mon 9/04/23															
309	Evaluation Committee Meeting #1 (Date TBC by FHA)	1 day	Tue 9/05/23	Tue 9/05/23	308														
310	Incorporate Feedback from Evaluation Meeting #1	10 days	Wed 9/06/23	Tue 9/19/23	309														
311	Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development) by FHA	1 day	Wed 9/20/23	Wed 9/20/23	310														
312	Evaluation Committee Meeting #2 (Date TBC by FHA)	1 day	Thu 9/21/23	Thu 9/21/23	311														
313	Incorporate Feedback from Evaluation Meeting #2	1 day	Fri 9/22/23	Fri 9/22/23	312														
314	RFP Documents Preparation by ED FED	4 days	Mon 9/25/23	Thu 9/28/23	313														
315	Release RFP Document Draft to FHA by ED FED	0 days	Thu 9/28/23	Thu 9/28/23	314														
316	Owner Review of Draft documents	1 wk	Fri 9/29/23	Thu 10/05/23	315														
317	RFP Documents Preparation Meeting#1 - Review RFP draft (Date TBC by FHA)	1 day	Fri 10/06/23	Fri 10/06/23	316														
318	Incorporate Feedback from RFP Documents Preparation Meeting#1	1 day	Mon 10/09/23	Mon 10/09/23	317														
319	Approval of all Documentation incl Final Specs, D&C Drawings, etc	1 day	Tue 10/10/23	Tue 10/10/23	318														
320	Tender Period	14 days	Wed 10/11/23	Mon 10/30/23															
321	Open Tender Period (RFP/RFQ/Direct Awards)	11 days	Wed 10/11/23	Wed 10/25/23	319														
322	Tender Process Close	0 days	Wed 10/25/23	Wed 10/25/23	321														
323	Proposal Completeness Check	2 days	Thu 10/26/23	Fri 10/27/23	322														
324	Technical Compliance Check	2 days	Thu 10/26/23	Fri 10/27/23	322														
325	Financial Analysis	2 days	Thu 10/26/23	Fri 10/27/23	322														
326	Financial Analysis Complete	0 days	Fri 10/27/23	Fri 10/27/23	325														
327	Prepare Procurement Summary Report	1 day	Mon 10/30/23	Mon 10/30/23	326														
328	Submit Procurement Summary Report to Owner (Short list) by ED FED	0 days	Mon 10/30/23	Mon 10/30/23	327														
329	RFP Evaluation Period	6 days	Tue 10/31/23	Tue 11/07/23															
330	Owner Review of Vendor Bids and Analysis by FHA	1 wk	Tue 10/31/23	Mon 11/06/23	328														
331	Owner Sign Off (Preferred Vendor)	1 day	Tue 11/07/23	Tue 11/07/23	330														
332	Contract Administration	5 days	Wed 11/08/23	Tue 11/14/23															
333	Final Negotiation with Successful Bidder by ED FED	1 wk	Wed 11/08/23	Tue 11/14/23	331														
334	Development of Equipment Configuration with ED FED	1 wk	Wed 11/08/23	Tue 11/14/23	331														

ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
335	Development of PO Documentations by EDDB	1 wk	Wed 11/08/23	Tue 11/14/23	331														
336	Collection of Signatures for Approval (Senior Leadership)	1 wk	Wed 11/08/23	Tue 11/14/23	331														
337	PO Issued by EDDB	0 days	Tue 11/14/23	Tue 11/14/23	336														
338	Final Design Coordination	5 days	Wed 11/08/23	Tue 11/14/23															
339	Coordination of Final Shop Drawing with Vendor	1 wk	Wed 11/08/23	Tue 11/14/23	331														
340	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Tue 11/14/23	Tue 11/14/23	339														
341	Shop Drawing Review by EDDB	1 wk	Wed 11/08/23	Tue 11/14/23	331														
342	Final Shop Drawing and Building Services Review Complete	0 days	Tue 11/14/23	Tue 11/14/23	341														
343	Final Shop Drawing Owner Review Period	1 wk	Wed 11/08/23	Tue 11/14/23	331														
344	Approval of Final Shop Drawings by Owner	0 days	Tue 11/14/23	Tue 11/14/23	343														
345	Delivery & Instalation	55 days	Wed 11/15/23	Fri 2/02/24															
346	Manufacturing & Site Coordination	45 days	Wed 11/15/23	Fri 1/19/24															
347	Fabrication and Confirm Delivery Room Readiness	8 wks	Wed 11/15/23	Fri 1/12/24	344														
348	Assembly, Installation, Set up and Testing (tied to room readiness dates)	1 wk	Mon 1/15/24	Fri 1/19/24	347														
349	Installation Complete- Issue Notice to Contracting Authority	0 days	Fri 1/19/24	Fri 1/19/24	348														
350	Vendor Closeout	10 days	Mon 1/22/24	Fri 2/02/24															
351	Contracting Authority Technical Acceptance testing/training	1 wk	Mon 1/22/24	Fri 1/26/24	349														
352	Collection and handover of Product Information(warranty, test reports, etc.)	1 wk	Mon 1/29/24	Fri 2/02/24	351														
353	Deficiencies & Remediation Period	1 wk	Mon 1/22/24	Fri 1/26/24	351SS														
354	Technical Acceptance and Training Complete	0 days	Fri 1/26/24	Fri 1/26/24	353														
355	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	1 wk	Mon 1/29/24	Fri 2/02/24	354														
356	FF&E Complete - Contracting Authority Sign Off	0 days	Fri 2/02/24	Fri 2/02/24	355														
357	6.2 Human Resources -Not In Contract (Category 1,2,3)- procurement by By FHA	186 days	Tue 5/16/23	Fri 2/02/24															
358	Procurement Strategy and Administration by FHA	41 days	Tue 5/16/23	Tue 7/11/23															
359	Coordinate Kick Off Strategy Meeting (Evaluation Committee, Formation, Shedules)	1 wk	Tue 5/16/23	Mon 5/22/23															
360	Kick Off Meeting (Date TBD)	0 days	Mon 5/22/23	Mon 5/22/23	359														
361	FHA to host Evaluation Committee Meeting #1 Prep (Building Documents incl.specs development)	2 wks	Tue 5/23/23	Mon 6/05/23	360														
362	Evaluation Committee Meeting #1 (Date TBD)	3 days	Tue 6/06/23	Thu 6/08/23	361														
363	FHA to Incorporate Feedback from Evaluation Meeting #1	5 days	Fri 6/09/23	Thu 6/15/23	362														
364	FHA To Release Documents to User Groups	0 days	Thu 6/15/23	Thu 6/15/23	363														
365	Owner Review of Bid Documents and Spec Sheets	5 days	Fri 6/16/23	Thu 6/22/23	364														
366	FHA to host Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development)	1 wk	Fri 6/23/23	Thu 6/29/23	365														
367	Evaluation Committee Meeting #2 (Date TBD)	3 days	Fri 6/30/23	Tue 7/04/23	366														
368	FHA To Release Release Documents to User Groups	0 days	Tue 7/04/23	Tue 7/04/23	367														
369	FHA to Develop final set of Bid Documents incl Final Specs, D&C Drawings, etc.	1 wk	Wed 7/05/23	Tue 7/11/23	368														
370	Approval of all Documentation	0 days	Tue 7/11/23	Tue 7/11/23	369														
371	Tender Period by FHA	55 days	Wed 7/12/23	Tue 9/26/23															
372	Open Tender Period (RFP/RFQ/Direct Awards)	35 days	Wed 7/12/23	Tue 8/29/23	370SS														
373	Tender Process Close and Completeness Check	1 wk	Wed 8/30/23	Tue 9/05/23	372														
374	Technical Compliance Check	1 wk	Wed 9/06/23	Tue 9/12/23	373														
375	Technical Compliance Check Complete	0 days	Tue 9/12/23	Tue 9/12/23	374														
376	FinancialAnalysis	1 wk	Wed 9/13/23	Tue 9/19/23	375														
377	Financial Analysis Complete	0 days	Tue 9/19/23	Tue 9/19/23	376														
378	Prepare Procurement Summary Report	5 days	Wed 9/20/23	Tue 9/26/23	377														
379	Submit Procurement Summary Report to FHA Senior Leadership (Shortlist to EDDB)	0 days	Tue 9/26/23	Tue 9/26/23	378														
380	RFP Evaluation Period by FHA	34 days	Wed 9/13/23	Mon 10/30/23															
381	Owner Review of Vendor Bids and Analysis by FHA	1 wk	Wed 9/13/23	Tue 9/19/23	375SS														
382	Evaluation Committee Meeting #3 for Tender Analysis and Vendor Shortlist (Date TBD)	2 days	Wed 9/27/23	Thu 9/28/23	379,381														
383	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	1 wk	Fri 9/29/23	Thu 10/05/23	382														
384	Vendor Presentations, Site Visits, On-Site Evaluations, etc.by	1 wk	Fri 10/06/23	Thu 10/12/23	383														
385	Organize User Feedback and Tabulate Scores	1 wk	Fri 10/13/23	Thu 10/19/23	384														
386	Evaluation Committee Meeting #5 for Final Vendor Selection (Date TBD)	2 days	Fri 10/20/23	Mon 10/23/23	385														
387	Submit Final Procurement Report to Senior Leadership for Sign Off	0 days	Mon 10/23/23	Mon 10/23/23	386														
388	Owner Review Period	5 days	Tue 10/24/23	Mon 10/30/23	387														
389	Owner Sign Off (Preferred Vendor & Notification to ED FED)	0 days	Mon 10/30/23	Mon 10/30/23	388														
390	Contract Administration by FHA	5 days	Tue 10/31/23	Mon 11/06/23															
391	Final Negotiation with Successful Bidder	1 wk	Tue 10/31/23	Mon 11/06/23	389														
392	Development of Equipment Configuration	1 wk	Tue 10/31/23	Mon 11/06/23	389														
393	Development of PO Documentations by FHA	1 wk	Tue 10/31/23	Mon 11/06/23	389														
394	Collection of Signatures for Approval (Senior Leadership)	1 wk	Tue 10/31/23	Mon 11/06/23	389														
395	PO Issued by Owner	0 days	Mon 11/06/23	Mon 11/06/23	394														
396	Final Design Coordination by FHA	5 days	Tue 11/07/23	Mon 11/13/23															
397	Coordination of Final Shop Drawing with Vendor	5 days	Tue 11/07/23	Mon 11/13/23	395														
398	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Mon 11/13/23	Mon 11/13/23	397														
399	Shop Drawing Review by EDDB	1 wk	Tue 11/07/23	Mon 11/13/23	395														
400	Final Shop Drawing and Building Services Review Complete	0 days	Mon 11/13/23	Mon 11/13/23	399														
401	Delivery & Installation by FHA, Vendor or EDDB	55 days	Wed 11/15/23	Fri 2/02/24															

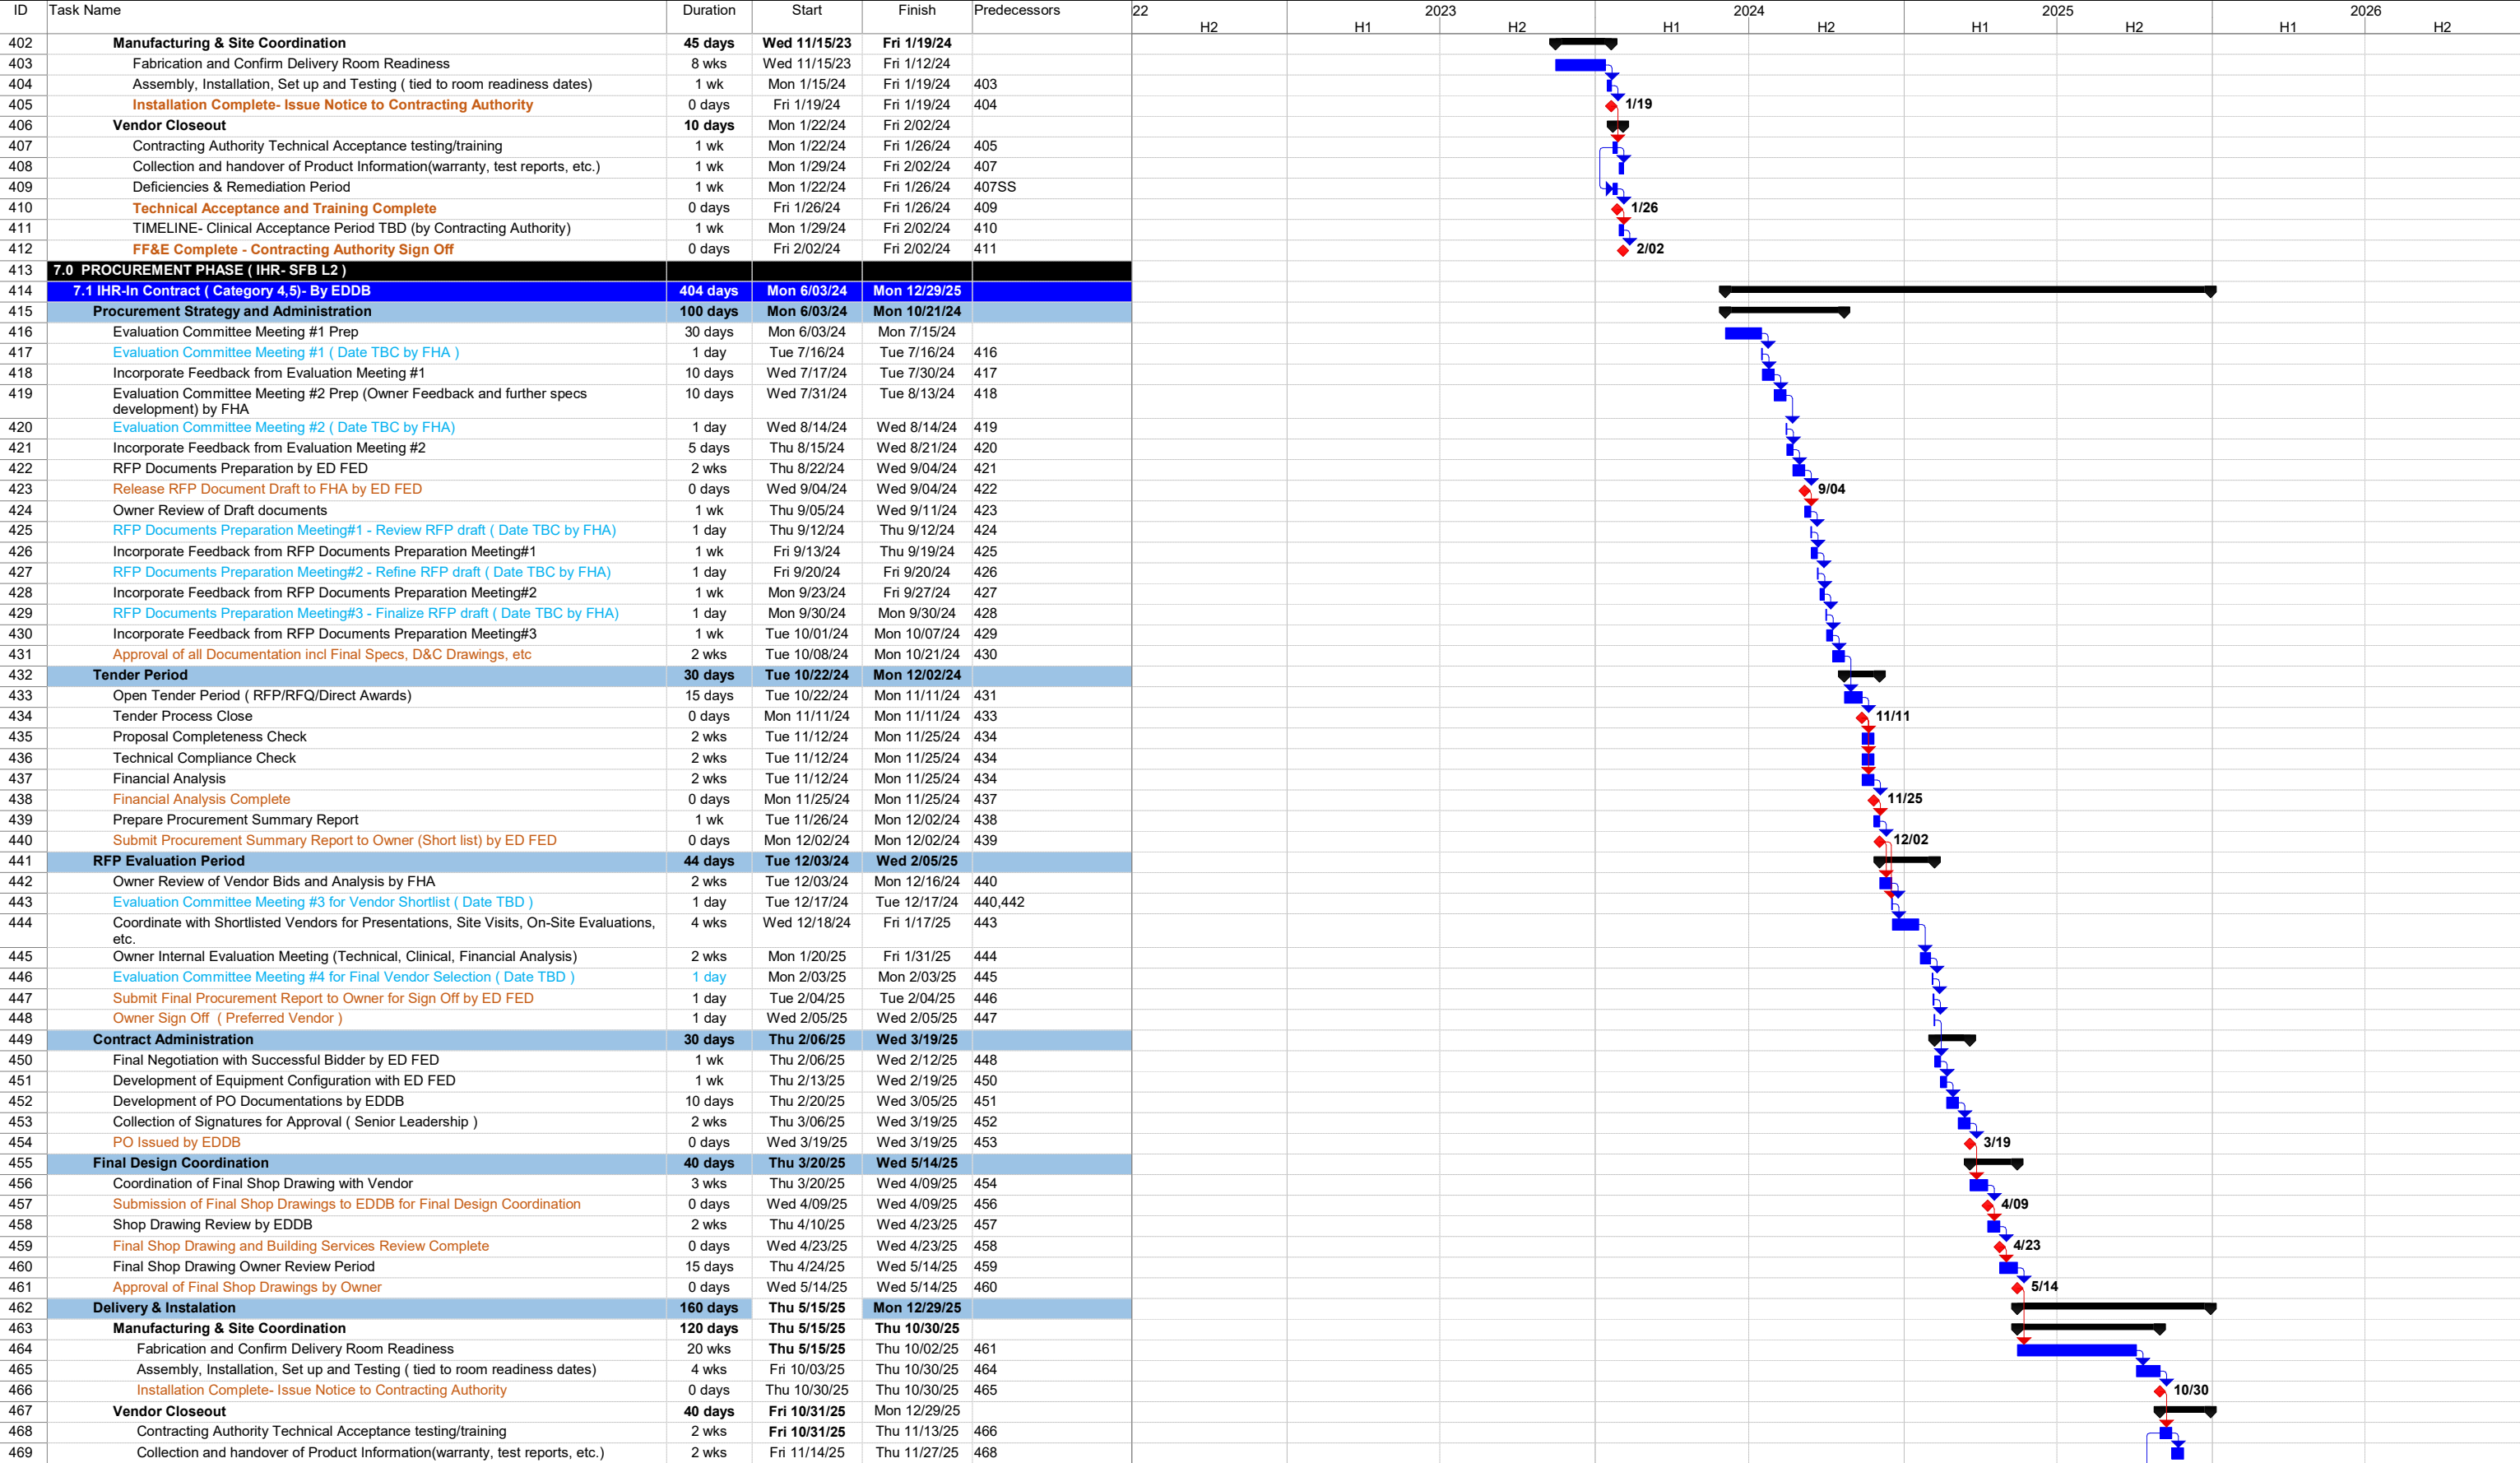

ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
470	Deficiencies & Remediation Period	4 wks	Fri 10/31/25	Thu 11/27/25	468SS														
471	Technical Acceptance and Training Complete	0 days	Thu 11/27/25	Thu 11/27/25	470														
472	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	4 wks	Fri 11/28/25	Mon 12/29/25	471														
473	FF&E Complete - Contracting Authority Sign Off	0 days	Mon 12/29/25	Mon 12/29/25	472														
474	7.2 IHR-Not In Contract (Category 1,2,3)- procurement by By FHA	380 days	Mon 7/08/24	Mon 12/29/25															
475	Procurement Strategy and Administration by FHA	46 days	Mon 7/08/24	Mon 9/09/24															
476	Coordinate Kick Off Strategy Meeting (Evaluation Committee, Formation, Schedules)	1 wk	Mon 7/08/24	Fri 7/12/24															
477	Kick Off Meeting (Date TBD)	0 days	Fri 7/12/24	Fri 7/12/24	476														
478	FHA to host Evaluation Committee Meeting #1 Prep (Building Documents incl.specs development)	2 wks	Mon 7/15/24	Fri 7/26/24	477														
479	Evaluation Committee Meeting #1 (Date TBD)	3 days	Mon 7/29/24	Wed 7/31/24	478														
480	FHA to Incorporate Feedback from Evaluation Meeting #1	5 days	Thu 8/01/24	Wed 8/07/24	479														
481	FHA To Release Documents to User Groups	0 days	Wed 8/07/24	Wed 8/07/24	480														
482	Owner Review of Bid Documents and Spec Sheets	10 days	Thu 8/08/24	Wed 8/21/24	481														
483	FHA to host Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development)	1 wk	Thu 8/22/24	Wed 8/28/24	482														
484	Evaluation Committee Meeting #2 (Date TBD)	3 days	Thu 8/29/24	Mon 9/02/24	483														
485	FHA To Release Release Documents to User Groups	0 days	Mon 9/02/24	Mon 9/02/24	484														
486	FHA to Develop final set of Bid Documents incl Final Specs, D&C Drawings, etc.	1 wk	Tue 9/03/24	Mon 9/09/24	485														
487	Approval of all Documentation	0 days	Mon 9/09/24	Mon 9/09/24	486														
488	Tender Period by FHA	55 days	Tue 9/10/24	Mon 11/25/24															
489	Open Tender Period (RFP/RFQ/Direct Awards)	35 days	Tue 9/10/24	Mon 10/28/24	487SS														
490	Tender Process Close and Completeness Check	1 wk	Tue 10/29/24	Mon 11/04/24	489														
491	Technical Compliance Check	1 wk	Tue 11/05/24	Mon 11/11/24	490														
492	Technical Compliance Check Complete	0 days	Mon 11/11/24	Mon 11/11/24	491														
493	FinancialAnalysis	1 wk	Tue 11/12/24	Mon 11/18/24	492														
494	Financial Analysis Complete	0 days	Mon 11/18/24	Mon 11/18/24	493														
495	Prepare Procurement Summary Report	5 days	Tue 11/19/24	Mon 11/25/24	494														
496	Submit Procurement Summary Report to FHA Senior Leadership (Shortlist to EDDB)	0 days	Mon 11/25/24	Mon 11/25/24	495														
497	RFP Evaluation Period by FHA	49 days	Tue 11/12/24	Wed 1/22/25															
498	Owner Review of Vendor Bids and Analysis by FHA	3 wks	Tue 11/12/24	Mon 12/02/24	492SS														
499	Evaluation Committee Meeting #4 for Tender Analysis and Vendor Shortlist (Date TBD)	2 days	Tue 12/03/24	Wed 12/04/24	496,498														
500	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	2 wks	Thu 12/05/24	Wed 12/18/24	499														
501	Vendor Presentations, Site Visits, On-Site Evaluations, etc.by	1 wk	Thu 12/19/24	Fri 12/27/24	500														
502	Organize User Feedback and Tabulate Scores	1 wk	Mon 12/30/24	Mon 1/06/25	501														
503	Evaluation Committee Meeting #5 for Final Vendor Selection (Date TBD)	2 days	Tue 1/07/25	Wed 1/08/25	502														
504	Submit Final Procurement Report to Senior Leadership for Sign Off	0 days	Wed 1/08/25	Wed 1/08/25	503														
505	Owner Review Period	10 days	Thu 1/09/25	Wed 1/22/25	504														
506	Owner Sign Off (Preferred Vendor & Notification to ED FED)	0 days	Wed 1/22/25	Wed 1/22/25	505														
507	Contract Administration by FHA	45 days	Thu 1/23/25	Wed 3/26/25															
508	Final Negotiation with Successful Bidder	3 wks	Thu 1/23/25	Wed 2/12/25	506														
509	Development of Equipment Configuration	2 wks	Thu 2/13/25	Wed 2/26/25	508														
510	Development of PO Documentations by FHA	15 days	Thu 2/27/25	Wed 3/19/25	509														
511	Collection of Signatures for Approval (Senior Leadership)	1 wk	Thu 3/20/25	Wed 3/26/25	510														
512	PO Issued by Owner	0 days	Wed 3/26/25	Wed 3/26/25	511														
513	Final Design Coordination by FHA	35 days	Thu 3/27/25	Wed 5/14/25															
514	Coordination of Final Shop Drawing with Vendor	4 wks	Thu 3/27/25	Wed 4/23/25	512														
515	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Wed 4/23/25	Wed 4/23/25	514														
516	Shop Drawing Review by EDDB	3 wks	Thu 4/24/25	Wed 5/14/25	515														
517	Final Shop Drawing and Building Services Review Complete	0 days	Wed 5/14/25	Wed 5/14/25	516														
518	Delivery & Installation by FHA, Vendor or EDDB	160 days	Thu 5/15/25	Mon 12/29/25															
519	Manufacturing & Site Coordination	120 days	Thu 5/15/25	Thu 10/30/25															
520	Fabrication and Confirm Delivery Room Readiness	20 wks	Thu 5/15/25	Thu 10/02/25	517														
521	Assembly, Installation, Set up and Testing (tied to room readiness dates)	4 wks	Fri 10/03/25	Thu 10/30/25	520														
522	Installation Complete- Issue Notice to Contracting Authority	0 days	Thu 10/30/25	Thu 10/30/25	521														
523	Vendor Closeout	40 days	Fri 10/31/25	Mon 12/29/25															
524	Contracting Authority Technical Acceptance testing/training	2 wks	Fri 10/31/25	Thu 11/13/25	522														
525	Collection and handover of Product Information(warranty, test reports, etc.)	2 wks	Fri 11/14/25	Thu 11/27/25	524														
526	Deficiencies & Remediation Period	4 wks	Fri 10/31/25	Thu 11/27/25	524SS														
527	Technical Acceptance and Training Complete	0 days	Thu 11/27/25	Thu 11/27/25	526														
528	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	4 wks	Fri 11/28/25	Mon 12/29/25	527														
529	FF&E Complete - Contracting Authority Sign Off	0 days	Mon 12/29/25	Mon 12/29/25	528														
530	8.0 PROCUREMENT PHASE (EMERGENCY - SFB L3)																		
531	8.1 EMERGENCY -In Contract (Category 4,5)- By EDDB	424 days	Tue 6/11/24	Wed 2/04/26															
532	Procurement Strategy and Administration	95 days	Tue 6/11/24	Tue 10/22/24															
533	Evaluation Committee Meeting #1 Prep	30 days	Tue 6/11/24	Tue 7/23/24															
534	Evaluation Committee Meeting #1 (Date TBC by FHA)	1 day	Wed 7/24/24	Wed 7/24/24	533														
535	Incorporate Feedback from Evaluation Meeting #1	10 days	Thu 7/25/24	Wed 8/07/24	534														

ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
536	Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development) by FHA	10 days	Thu 8/08/24	Wed 8/21/24	535														
537	Evaluation Committee Meeting #2 (Date TBC by FHA)	1 day	Thu 8/22/24	Thu 8/22/24	536														
538	Incorporate Feedback from Evaluation Meeting #2	5 days	Fri 8/23/24	Thu 8/29/24	537														
539	RFP Documents Preparation by ED FED	1 wk	Fri 8/30/24	Thu 9/05/24	538														
540	Release RFP Document Draft to FHA by ED FED	0 days	Thu 9/05/24	Thu 9/05/24	539														
541	Owner Review of Draft documents	1 wk	Fri 9/06/24	Thu 9/12/24	540														
542	RFP Documents Preparation Meeting#1 - Review RFP draft (Date TBC by FHA)	1 day	Fri 9/13/24	Fri 9/13/24	541														
543	Incorporate Feedback from RFP Documents Preparation Meeting#1	1 wk	Mon 9/16/24	Fri 9/20/24	542														
544	RFP Documents Preparation Meeting#2 - Refine RFP draft (Date TBC by FHA)	1 day	Mon 9/23/24	Mon 9/23/24	543														
545	Incorporate Feedback from RFP Documents Preparation Meeting#2	1 wk	Tue 9/24/24	Mon 9/30/24	544														
546	RFP Documents Preparation Meeting#3 - Finalize RFP draft (Date TBC by FHA)	1 day	Tue 10/01/24	Tue 10/01/24	545														
547	Incorporate Feedback from RFP Documents Preparation Meeting#3	1 wk	Wed 10/02/24	Tue 10/08/24	546														
548	Approval of all Documentation incl Final Specs, D&C Drawings, etc	2 wks	Wed 10/09/24	Tue 10/22/24	547														
549	Tender Period	30 days	Wed 10/23/24	Tue 12/03/24															
550	Open Tender Period (RFP/RFQ/Direct Awards)	15 days	Wed 10/23/24	Tue 11/12/24	548														
551	Tender Process Close	0 days	Tue 11/12/24	Tue 11/12/24	550														
552	Proposal Completeness Check	2 wks	Wed 11/13/24	Tue 11/26/24	551														
553	Technical Compliance Check	2 wks	Wed 11/13/24	Tue 11/26/24	551														
554	Financial Analysis	2 wks	Wed 11/13/24	Tue 11/26/24	551														
555	Financial Analysis Complete	0 days	Tue 11/26/24	Tue 11/26/24	554														
556	Prepare Procurement Summary Report	1 wk	Wed 11/27/24	Tue 12/03/24	555														
557	Submit Procurement Summary Report to Owner (Short list) by ED FED	0 days	Tue 12/03/24	Tue 12/03/24	556														
558	RFP Evaluation Period	44 days	Wed 12/04/24	Thu 2/06/25															
559	Owner Review of Vendor Bids and Analysis by FHA	2 wks	Wed 12/04/24	Tue 12/17/24	557														
560	Evaluation Committee Meeting #3 for Vendor Shortlist (Date TBD)	1 day	Wed 12/18/24	Wed 12/18/24	557,559														
561	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	4 wks	Thu 12/19/24	Mon 1/20/25	560														
562	Owner Internal Evaluation Meeting (Technical, Clinical, Financial Analysis)	2 wks	Tue 1/21/25	Mon 2/03/25	561														
563	Evaluation Committee Meeting #4 for Final Vendor Selection (Date TBD)	1 day	Tue 2/04/25	Tue 2/04/25	562														
564	Submit Final Procurement Report to Owner for Sign Off by ED FED	1 day	Wed 2/05/25	Wed 2/05/25	563														
565	Owner Sign Off (Preferred Vendor)	1 day	Thu 2/06/25	Thu 2/06/25	564														
566	Contract Administration	30 days	Fri 2/07/25	Thu 3/20/25															
567	Final Negotiation with Successful Bidder by ED FED	1 wk	Fri 2/07/25	Thu 2/13/25	565														
568	Development of Equipment Configuration with ED FED	1 wk	Fri 2/14/25	Thu 2/20/25	567														
569	Development of PO Documentations by EDDB	10 days	Fri 2/21/25	Thu 3/06/25	568														
570	Collection of Signatures for Approval (Senior Leadership)	2 wks	Fri 3/07/25	Thu 3/20/25	569														
571	PO Issued by EDDB	0 days	Thu 3/20/25	Thu 3/20/25	570														
572	Final Design Coordination	40 days	Fri 3/21/25	Thu 5/15/25															
573	Coordination of Final Shop Drawing with Vendor	3 wks	Fri 3/21/25	Thu 4/10/25	571														
574	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Thu 4/10/25	Thu 4/10/25	573														
575	Shop Drawing Review by EDDB	2 wks	Fri 4/11/25	Thu 4/24/25	574														
576	Final Shop Drawing and Building Services Review Complete	0 days	Thu 4/24/25	Thu 4/24/25	575														
577	Final Shop Drawing Owner Review Period	15 days	Fri 4/25/25	Thu 5/15/25	576														
578	Approval of Final Shop Drawings by Owner	0 days	Thu 5/15/25	Thu 5/15/25	577														
579	Delivery & Instalation	185 days	Fri 5/16/25	Wed 2/04/26															
580	Manufacturing & Site Coordination	145 days	Fri 5/16/25	Fri 12/05/25															
581	Fabrication and Confirm Delivery Room Readiness	20 wks	Fri 5/16/25	Fri 10/03/25	578														
582	Assembly, Installation, Set up and Testing (tied to room readiness dates)	9 wks	Mon 10/06/25	Fri 12/05/25	581														
583	Installation Complete- Issue Notice to Contracting Authority	0 days	Fri 12/05/25	Fri 12/05/25	582														
584	Vendor Closeout	40 days	Mon 12/08/25	Wed 2/04/26															
585	Contracting Authority Technical Acceptance testing/training	2 wks	Mon 12/08/25	Fri 12/19/25	583														
586	Collection and handover of Product Information(warranty, test reports, etc.)	2 wks	Mon 12/22/25	Wed 1/07/26	585														
587	Deficiencies & Remediation Period	4 wks	Mon 12/08/25	Wed 1/07/26	585SS														
588	Technical Acceptance and Training Complete	0 days	Wed 1/07/26	Wed 1/07/26	587														
589	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	4 wks	Thu 1/08/26	Wed 2/04/26	588														
590	FF&E Complete - Contracting Authority Sign Off	0 days	Wed 2/04/26	Wed 2/04/26	589														
591	8.2 EMERGENCY-Not In Contract (Category 1,2,3)- procurement by By FHA	405 days	Tue 7/02/24	Wed 1/28/26															
592	Procurement Strategy and Administration by FHA	46 days	Tue 7/02/24	Tue 9/03/24															
593	Coordinate Kick Off Strategy Meeting (Evaluation Committee, Formation, Shedules)	1 wk	Tue 7/02/24	Mon 7/08/24															
594	Kick Off Meeting (Date TBD)	0 days	Mon 7/08/24	Mon 7/08/24	593														
595	FHA to host Evaluation Committee Meeting #1 Prep (Building Documents incl.specs development)	2 wks	Tue 7/09/24	Mon 7/22/24	594														
596	Evaluation Committee Meeting #1 (Date TBD)	3 days	Tue 7/23/24	Thu 7/25/24	595														
597	FHA to Incorporate Feedback from Evaluation Meeting #1	5 days	Fri 7/26/24	Thu 8/01/24	596														
598	FHA To Release Documents to User Groups	0 days	Thu 8/01/24	Thu 8/01/24	597														
599	Owner Review of Bid Documents and Spec Sheets	10 days	Fri 8/02/24	Thu 8/15/24	598														
600	FHA to host Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development)	1 wk	Fri 8/16/24	Thu 8/22/24	599														
601	Evaluation Committee Meeting #2 (Date TBD)	3 days	Fri 8/23/24	Tue 8/27/24	600														
602	FHA To Release Release Documents to User Groups	0 days	Tue 8/27/24	Tue 8/27/24	601														

ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
603	FHA to Develop final set of Bid Documents incl Final Specs, D&C Drawings, etc.	1 wk	Wed 8/28/24	Tue 9/03/24	602														
604	Approval of all Documentation	0 days	Tue 9/03/24	Tue 9/03/24	603														
605	Tender Period by FHA	55 days	Wed 9/04/24	Tue 11/19/24															
606	Open Tender Period (RFP/RFQ/Direct Awards)	35 days	Wed 9/04/24	Tue 10/22/24	604SS														
607	Tender Process Close and Completeness Check	1 wk	Wed 10/23/24	Tue 10/29/24	606														
608	Technical Compliance Check	1 wk	Wed 10/30/24	Tue 11/05/24	607														
609	Technical Compliance Check Complete	0 days	Tue 11/05/24	Tue 11/05/24	608														
610	FinancialAnalysis	1 wk	Wed 11/06/24	Tue 11/12/24	609														
611	Financial Analysis Complete	0 days	Tue 11/12/24	Tue 11/12/24	610														
612	Prepare Procurement Summary Report	5 days	Wed 11/13/24	Tue 11/19/24	611														
613	Submit Procurement Summary Report to FHA Senior Leadership (Shortlist to EDDB)	0 days	Tue 11/19/24	Tue 11/19/24	612														
614	RFP Evaluation Period by FHA	49 days	Wed 11/06/24	Thu 1/16/25															
615	Owner Review of Vendor Bids and Analysis by FHA	3 wks	Wed 11/06/24	Tue 11/26/24	609SS														
616	Evaluation Committee Meeting #4 for Tender Analysis and Vendor Shortlist (Date TBD)	2 days	Wed 11/27/24	Thu 11/28/24	613,615														
617	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	2 wks	Fri 11/29/24	Thu 12/12/24	616														
618	Vendor Presentations, Site Visits, On-Site Evaluations, etc.by	1 wk	Fri 12/13/24	Thu 12/19/24	617														
619	Organize User Feedback and Tabulate Scores	1 wk	Fri 12/20/24	Mon 12/30/24	618														
620	Evaluation Committee Meeting #5 for Final Vendor Selection (Date TBD)	2 days	Tue 12/31/24	Thu 1/02/25	619														
621	Submit Final Procurement Report to Senior Leadership for Sign Off	0 days	Thu 1/02/25	Thu 1/02/25	620														
622	Owner Review Period	10 days	Fri 1/03/25	Thu 1/16/25	621														
623	Owner Sign Off (Preferred Vendor & Notification to ED FED)	0 days	Thu 1/16/25	Thu 1/16/25	622														
624	Contract Administration by FHA	45 days	Fri 1/17/25	Thu 3/20/25															
625	Final Negotiation with Successful Bidder	3 wks	Fri 1/17/25	Thu 2/06/25	623														
626	Development of Equipment Configuration	2 wks	Fri 2/07/25	Thu 2/20/25	625														
627	Development of PO Documentations by FHA	15 days	Fri 2/21/25	Thu 3/13/25	626														
628	Collection of Signatures for Approval (Senior Leadership)	1 wk	Fri 3/14/25	Thu 3/20/25	627														
629	PO Issued by Owner	0 days	Thu 3/20/25	Thu 3/20/25	628														
630	Final Design Coordination by FHA	35 days	Fri 3/21/25	Thu 5/08/25															
631	Coordination of Final Shop Drawing with Vendor	4 wks	Fri 3/21/25	Thu 4/17/25	629														
632	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Thu 4/17/25	Thu 4/17/25	631														
633	Shop Drawing Review by EDDB	3 wks	Fri 4/18/25	Thu 5/08/25	632														
634	Final Shop Drawing and Building Services Review Complete	0 days	Thu 5/08/25	Thu 5/08/25	633														
635	Delivery & Installation by FHA, Vendor or EDDB	185 days	Fri 5/09/25	Wed 1/28/26															
636	Manufacturing & Site Coordination	145 days	Fri 5/09/25	Fri 11/28/25															
637	Fabrication and Confirm Delivery Room Readiness	20 wks	Fri 5/09/25	Fri 9/26/25	634														
638	Assembly, Installation, Set up and Testing (tied to room readiness dates)	9 wks	Mon 9/29/25	Fri 11/28/25	637														
639	Installation Complete- Issue Notice to Contracting Authority	0 days	Fri 11/28/25	Fri 11/28/25	638														
640	Vendor Closeout	40 days	Mon 12/01/25	Wed 1/28/26															
641	Contracting Authority Technical Acceptance testing/training	2 wks	Mon 12/01/25	Fri 12/12/25	639														
642	Collection and handover of Product Information(warranty, test reports, etc.)	2 wks	Mon 12/15/25	Tue 12/30/25	641														
643	Deficiencies & Remediation Period	4 wks	Mon 12/01/25	Tue 12/30/25	641SS														
644	Technical Acceptance and Training Complete	0 days	Tue 12/30/25	Tue 12/30/25	643														
645	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	4 wks	Wed 12/31/25	Wed 1/28/26	644														
646	FF&E Complete - Contracting Authority Sign Off	0 days	Wed 1/28/26	Wed 1/28/26	645														
647	9.0 PROCUREMENT PHASE (FMO SPACE - SFB L2)																		
648	9.1 FMO SPACE -In Contract (Category 4,5)- By EDDB	424 days	Thu 5/23/24	Fri 1/16/26															
649	Procurement Strategy and Administration	95 days	Thu 5/23/24	Thu 10/03/24															
650	Evaluation Committee Meeting #1 Prep	30 days	Thu 5/23/24	Thu 7/04/24															
651	Evaluation Committee Meeting #1 (Date TBC by FHA)	1 day	Fri 7/05/24	Fri 7/05/24	650														
652	Incorporate Feedback from Evaluation Meeting #1	10 days	Mon 7/08/24	Fri 7/19/24	651														
653	Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development) by FHA	10 days	Mon 7/22/24	Fri 8/02/24	652														
654	Evaluation Committee Meeting #2 (Date TBC by FHA)	1 day	Mon 8/05/24	Mon 8/05/24	653														
655	Incorporate Feedback from Evaluation Meeting #2	5 days	Tue 8/06/24	Mon 8/12/24	654														
656	RFP Documents Preparation by ED FED	1 wk	Tue 8/13/24	Mon 8/19/24	655														
657	Release RFP Document Draft to FHA by ED FED	0 days	Mon 8/19/24	Mon 8/19/24	656														
658	Owner Review of Draft documents	1 wk	Tue 8/20/24	Mon 8/26/24	657														
659	RFP Documents Preparation Meeting#1 - Review RFP draft (Date TBC by FHA)	1 day	Tue 8/27/24	Tue 8/27/24	658														
660	Incorporate Feedback from RFP Documents Preparation Meeting#1	1 wk	Wed 8/28/24	Tue 9/03/24	659														
661	RFP Documents Preparation Meeting#2 - Refine RFP draft (Date TBC by FHA)	1 day	Wed 9/04/24	Wed 9/04/24	660														
662	Incorporate Feedback from RFP Documents Preparation Meeting#2	1 wk	Thu 9/05/24	Wed 9/11/24	661														
663	RFP Documents Preparation Meeting#3 - Finalize RFP draft (Date TBC by FHA)	1 day	Thu 9/12/24	Thu 9/12/24	662														
664	Incorporate Feedback from RFP Documents Preparation Meeting#3	1 wk	Fri 9/13/24	Thu 9/19/24	663														
665	Approval of all Documentation incl Final Specs, D&C Drawings, etc	2 wks	Fri 9/20/24	Thu 10/03/24	664														
666	Tender Period	30 days	Fri 10/04/24	Thu 11/14/24															
667	Open Tender Period (RFP/RFQ/Direct Awards)	15 days	Fri 10/04/24	Thu 10/24/24	665														
668	Tender Process Close	0 days	Thu 10/24/24	Thu 10/24/24	667														
669	Proposal Completeness Check	2 wks	Fri 10/25/24	Thu 11/07/24	668														

ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
670	Technical Compliance Check	2 wks	Fri 10/25/24	Thu 11/07/24	668														
671	Financial Analysis	2 wks	Fri 10/25/24	Thu 11/07/24	668														
672	Financial Analysis Complete	0 days	Thu 11/07/24	Thu 11/07/24	671														
673	Prepare Procurement Summary Report	1 wk	Fri 11/08/24	Thu 11/14/24	672														
674	Submit Procurement Summary Report to Owner (Short list) by ED FED	0 days	Thu 11/14/24	Thu 11/14/24	673														
675	RFP Evaluation Period	44 days	Fri 11/15/24	Mon 1/20/25															
676	Owner Review of Vendor Bids and Analysis by FHA	2 wks	Fri 11/15/24	Thu 11/28/24	674														
677	Evaluation Committee Meeting #3 for Vendor Shortlist (Date TBD)	1 day	Fri 11/29/24	Fri 11/29/24	674,676														
678	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	4 wks	Mon 12/02/24	Tue 12/31/24	677														
679	Owner Internal Evaluation Meeting (Technical, Clinical, Financial Analysis)	2 wks	Thu 1/02/25	Wed 1/15/25	678														
680	Evaluation Committee Meeting #4 for Final Vendor Selection (Date TBD)	1 day	Thu 1/16/25	Thu 1/16/25	679														
681	Submit Final Procurement Report to Owner for Sign Off by ED FED	1 day	Fri 1/17/25	Fri 1/17/25	680														
682	Owner Sign Off (Preferred Vendor)	1 day	Mon 1/20/25	Mon 1/20/25	681														
683	Contract Administration	30 days	Tue 1/21/25	Mon 3/03/25															
684	Final Negotiation with Successful Bidder by ED FED	1 wk	Tue 1/21/25	Mon 1/27/25	682														
685	Development of Equipment Configuration with ED FED	1 wk	Tue 1/28/25	Mon 2/03/25	684														
686	Development of PO Documentations by EDDB	10 days	Tue 2/04/25	Mon 2/17/25	685														
687	Collection of Signatures for Approval (Senior Leadership)	2 wks	Tue 2/18/25	Mon 3/03/25	686														
688	PO Issued by EDDB	0 days	Mon 3/03/25	Mon 3/03/25	687														
689	Final Design Coordination	40 days	Tue 3/04/25	Mon 4/28/25															
690	Coordination of Final Shop Drawing with Vendor	3 wks	Tue 3/04/25	Mon 3/24/25	688														
691	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Mon 3/24/25	Mon 3/24/25	690														
692	Shop Drawing Review by EDDB	2 wks	Tue 3/25/25	Mon 4/07/25	691														
693	Final Shop Drawing and Building Services Review Complete	0 days	Mon 4/07/25	Mon 4/07/25	692														
694	Final Shop Drawing Owner Review Period	15 days	Tue 4/08/25	Mon 4/28/25	693														
695	Approval of Final Shop Drawings by Owner	0 days	Mon 4/28/25	Mon 4/28/25	694														
696	Delivery & Installation	185 days	Tue 4/29/25	Fri 1/16/26															
697	Manufacturing & Site Coordination	145 days	Tue 4/29/25	Tue 11/18/25															
698	Fabrication and Confirm Delivery Room Readiness	20 wks	Tue 4/29/25	Tue 9/16/25	695														
699	Assembly, Installation, Set up and Testing (tied to room readiness dates)	9 wks	Wed 9/17/25	Tue 11/18/25	698														
700	Installation Complete- Issue Notice to Contracting Authority	0 days	Tue 11/18/25	Tue 11/18/25	699														
701	Vendor Closeout	40 days	Wed 11/19/25	Fri 1/16/26															
702	Contracting Authority Technical Acceptance testing/training	2 wks	Wed 11/19/25	Tue 12/02/25	700														
703	Collection and handover of Product Information(warranty, test reports, etc.)	2 wks	Wed 12/03/25	Tue 12/16/25	702														
704	Deficiencies & Remediation Period	4 wks	Wed 11/19/25	Tue 12/16/25	702SS														
705	Technical Acceptance and Training Complete	0 days	Tue 12/16/25	Tue 12/16/25	704														
706	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	4 wks	Wed 12/17/25	Fri 1/16/26	705														
707	FF&E Complete - Contracting Authority Sign Off	0 days	Fri 1/16/26	Fri 1/16/26	706														
708	9.2 FMO SPACE-Not In Contract (Category 1,2,3)- procurement by By FHA	382 days	Mon 7/22/24	Thu 1/15/26															
709	Procurement Strategy and Administration by FHA	52 days	Mon 7/22/24	Tue 10/01/24															
710	Coordinate Kick Off Strategy Meeting (Evaluation Committee, Formation, Shedules)	1 wk	Mon 7/22/24	Fri 7/26/24															
711	Kick Off Meeting (Date TBD)	1 day	Mon 7/29/24	Mon 7/29/24	710														
712	FHA to host Evaluation Committee Meeting #1 Prep (Building Documents incl.specs development)	3 wks	Tue 7/30/24	Mon 8/19/24	711														
713	Evaluation Committee Meeting #1 (Date TBD)	3 days	Tue 8/20/24	Thu 8/22/24	712														
714	FHA to Incorporate Feedback from Evaluation Meeting #1	5 days	Fri 8/23/24	Thu 8/29/24	713														
715	FHA To Release Documents to User Groups	0 days	Thu 8/29/24	Thu 8/29/24	714														
716	Owner Review of Bid Documents and Spec Sheets	10 days	Fri 8/30/24	Thu 9/12/24	715														
717	FHA to host Evaluation Committee Meeting #2 Prep (Owner Feedback and further specs development)	1 wk	Fri 9/13/24	Thu 9/19/24	716														
718	Evaluation Committee Meeting #2 (Date TBD)	3 days	Fri 9/20/24	Tue 9/24/24	717														
719	FHA To Release Release Documents to User Groups	0 days	Tue 9/24/24	Tue 9/24/24	718														
720	FHA to Develop final set of Bid Documents incl Final Specs, D&C Drawings, etc.	1 wk	Wed 9/25/24	Tue 10/01/24	719														
721	Approval of all Documentation	0 days	Tue 10/01/24	Tue 10/01/24	720														
722	Tender Period by FHA	41 days	Wed 10/02/24	Wed 11/27/24															
723	Open Tender Period (RFP/RFQ/Direct Awards)	21 days	Wed 10/02/24	Wed 10/30/24	721SS														
724	Tender Process Close and Completeness Check	1 wk	Thu 10/31/24	Wed 11/06/24	723														
725	Technical Compliance Check	1 wk	Thu 11/07/24	Wed 11/13/24	724														
726	Technical Compliance Check Complete	0 days	Wed 11/13/24	Wed 11/13/24	725														
727	FinancialAnalysis	1 wk	Thu 11/14/24	Wed 11/20/24	726														
728	Financial Analysis Complete	0 days	Wed 11/20/24	Wed 11/20/24	727														
729	Prepare Procurement Summary Report	5 days	Thu 11/21/24	Wed 11/27/24	728														
730	Submit Procurement Summary Report to FHA Senior Leadership (Shortlist to EDDB)	0 days	Wed 11/27/24	Wed 11/27/24	729														
731	RFP Evaluation Period by FHA	49 days	Thu 11/14/24	Fri 1/24/25															
732	Owner Review of Vendor Bids and Analysis by FHA	3 wks	Thu 11/14/24	Wed 12/04/24	726SS														
733	Evaluation Committee Meeting #4 for Tender Analysis and Vendor Shortlist (Date TBD)	2 days	Thu 12/05/24	Fri 12/06/24	730,732														
734	Coordinate with Shortlisted Vendors for Presentations, Site Visits, On-Site Evaluations, etc.	2 wks	Mon 12/09/24	Fri 12/20/24	733														
735	Vendor Presentations, Site Visits, On-Site Evaluations, etc.by	1 wk	Mon 12/23/24	Tue 12/31/24	734														

ID	Task Name	Duration	Start	Finish	Predecessors	22	H2	H1	2023	H2	H1	2024	H2	H1	2025	H2	H1	2026	H2
736	Organize User Feedback and Tabulate Scores	1 wk	Thu 1/02/25	Wed 1/08/25	735														
737	Evaluation Committee Meeting #5 for Final Vendor Selection (Date TBD)	2 days	Thu 1/09/25	Fri 1/10/25	736														
738	Submit Final Procurement Report to Senior Leadership for Sign Off	0 days	Fri 1/10/25	Fri 1/10/25	737														
739	Owner Review Period	10 days	Mon 1/13/25	Fri 1/24/25	738														
740	Owner Sign Off (Preferred Vendor & Notification to ED FED)	0 days	Fri 1/24/25	Fri 1/24/25	739														
741	Contract Administration by FHA	35 days	Mon 1/27/25	Fri 3/14/25															
742	Final Negotiation with Successful Bidder	2 wks	Mon 1/27/25	Fri 2/07/25	740														
743	Development of Equipment Configuration	1 wk	Mon 2/10/25	Fri 2/14/25	742														
744	Development of PO Documentations by FHA	15 days	Mon 2/17/25	Fri 3/07/25	743														
745	Collection of Signatures for Approval (Senior Leadership)	1 wk	Mon 3/10/25	Fri 3/14/25	744														
746	PO Issued by Owner	0 days	Fri 3/14/25	Fri 3/14/25	745														
747	Final Design Coordination by FHA	30 days	Mon 3/17/25	Fri 4/25/25															
748	Coordination of Final Shop Drawing with Vendor	3 wks	Mon 3/17/25	Fri 4/04/25	746														
749	Submission of Final Shop Drawings to EDDB for Final Design Coordination	0 days	Fri 4/04/25	Fri 4/04/25	748														
750	Shop Drawing Review by EDDB	3 wks	Mon 4/07/25	Fri 4/25/25	749														
751	Final Shop Drawing and Building Services Review Complete	0 days	Fri 4/25/25	Fri 4/25/25	750														
752	Delivery & Installation by FHA, Vendor or EDDB	185 days	Mon 4/28/25	Thu 1/15/26															
753	Manufacturing & Site Coordination	145 days	Mon 4/28/25	Mon 11/17/25															
754	Fabrication and Confirm Delivery Room Readiness	20 wks	Mon 4/28/25	Mon 9/15/25	751														
755	Assembly, Installation, Set up and Testing (tied to room readiness dates)	9 wks	Tue 9/16/25	Mon 11/17/25	754														
756	Installation Complete- Issue Notice to Contracting Authority	0 days	Mon 11/17/25	Mon 11/17/25	755														
757	Vendor Closeout	40 days	Tue 11/18/25	Thu 1/15/26															
758	Contracting Authority Technical Acceptance testing/training	2 wks	Tue 11/18/25	Mon 12/01/25	756														
759	Collection and handover of Product Information(warranty, test reports, etc.)	2 wks	Tue 12/02/25	Mon 12/15/25	758														
760	Deficiencies & Remediation Period	4 wks	Tue 11/18/25	Mon 12/15/25	758SS														
761	Technical Acceptance and Training Complete	0 days	Mon 12/15/25	Mon 12/15/25	760														
762	TIMELINE- Clinical Acceptance Period TBD (by Contracting Authority)	4 wks	Tue 12/16/25	Thu 1/15/26	761														
763	FF&E Complete - Contracting Authority Sign Off	0 days	Thu 1/15/26	Thu 1/15/26	762														
